ID	Task Name	% Schedule	% Work Complete	Duration	Start	Finish
1	**Cadangan Mengantikan Alatubah Kepada Kilang Sedia Ada untuk Tetuan Vishay Semiconductor (M) Sdn Bhd**	**21%**	**0%**	**86 days**	**Tue 3/9/24**	**Tue 31/12/24**
2	Start	40%	35%	86 days	Tue 3/9/24	Tue 31/12/24
3	**Preliminaries**	**5%**	**0%**	**86 days**	**Tue 3/9/24**	**Tue 31/12/24**
4	**LV Electrrical Work**	0%	0%	21 days	Tue 3/9/24	Tue 1/10/24
5	Underground Mapping	0%	0%	4 days	Tue 10/9/24	Fri 13/9/24
6	Earthning And Lightning	0%	0%	19 days	Wed 4/9/24	Mon 30/9/24
7	Lighting And Power Point	0%	0%	19 days	Wed 4/9/24	Mon 30/9/24
8	**Equipment Delivery**	**0%**	**0%**	**50 days**	**Mon 7/10/24**	**Fri 13/12/24**
9	Transformer FAT	0%	0%	1 day	Mon 2/12/24	Mon 2/12/24
10	Transformer Delivery to Site	0%	0%	1 day	Tue 10/12/24	Tue 10/12/24
11	**Trunking / Cable Ladder Installation**	**65%**	**0%**	**4 days**	**Wed 11/12/24**	**Mon 16/12/24**
12	Install cable Tray and cable ladde	65%	0%	4 days	Wed 11/12/24	Mon 16/12/24
13	**Sub Main Cable**	**6%**	**0%**	**12 days**	**Mon 16/12/24**	**Tue 31/12/24**
14	Install Sub Main Cable	18%	0%	12 days	Mon 16/12/24	Tue 31/12/24
15	Install HT cable	0%	0%	12 days	Mon 16/12/24	Tue 31/12/24
16	Install Signal Cable	0%	0%	12 days	Mon 16/12/24	Tue 31/12/24

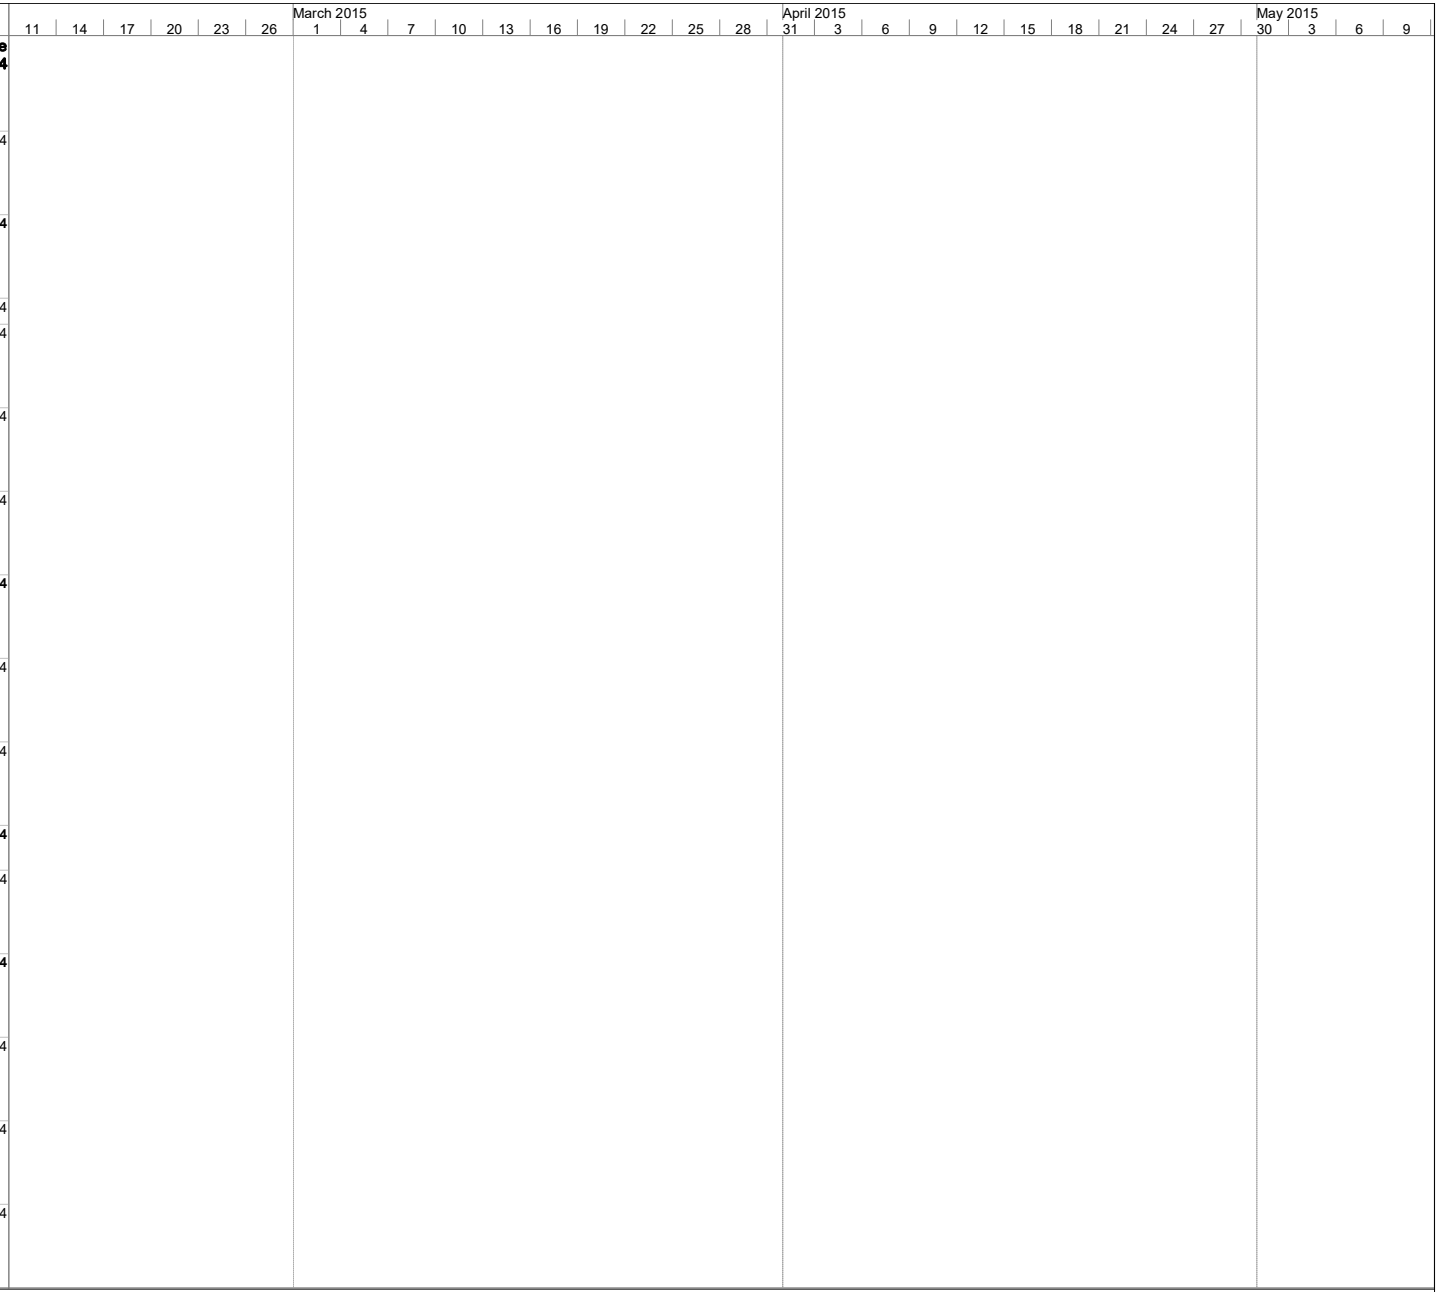

Project: Project1-min aik
Date: Thu 10/10/24

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Progress
Deadline
